e of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

urement Recorded On:

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
KSRRB 300-1 Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications(I No-19.1, P No-143), 8km lead						
RCC Drain						
Ambedkarnagara						
15th A cross Rd						
LHS(From Car Auto Spa)						
Ch:0.00m to 20.30m	1	20.30	1.50	1.20	36.54	
Ch:20.30m to 50.30m	1	30.00	1.50	1.20	54.00	
Ch:50.30m to 80.30m	1	30.00	1.50	1.20	54.00	
Ch:80.30m to 110.30m	1	30.00	1.50	1.20	54.00	
Ch:110.30m to 140.30m	1	30.00	1.50	1.20	54.00	
Ch:140.30m to 170.30m	1	30.00	1.50	1.20	54.00	
Ch:170.30m to 177.30m	1	7.00	1.50	1.20	12.60	
Road Gap						
Ch:177.30m to 204.40m	1	27.10				
Gap						
Ch:204.40m to 219.80m	1	15.40				
Gap						
Ch:219.80m to 241.80m	1	22.00				
Continue						
From (7th Main Rd)						
Ch:241.80m to 271.80m	1	30.00	1.50	1.20	54.00	
Ch:271.80m to 301.80m	1	30.00	1.50	1.20	54.00	
Ch:317.30m to 331.80m	1	30.00	1.50	1.20	54.00	
Chikbommasandra						
1st Main Rd						
RHS(From Main Rd)						
Ch:0.00m to 30.00m	1	30.00	1.80	1.20	64.80	
Culvert Gap						
Ch:30.00m to 51.00m	1	21.00	1.80	1.20	45.36	
Culvert Gap						
Ch:51.00m to 73.10m	1	22.10	1.80	1.20	47.74	
Culvert Gap						
Ch:73.10m to 100.60m	1	27.50	1.80	1.20	59.40	
Culvert Gap						

ractor

NEWZEN CONSULTANT Consultant Bangalore

Asst. Engineer

28/12/2020

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು

Asst. Executive Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
Ch:100.60m to 118.60m	1	18.00	1.80	1.20	38.88	
Temple Road						
Ch:0.00m to 30.00m	1	30.00	1.80	1.20	64.80	
Ch:30.00m to 51.00m	1	21.00	1.80	1.20	45.36	
Ambedkarnagara						
Ch:0.00m to 30.00m	1	30.00	1.10	1.10	36.30	
Ch:30.00m to 60.00m	1	30.00	1.10	1.10	36.30	
Ch:60.00m to 80.00m	1	20.00	1.10	1.10	24.20	
RCC Culvert						
Chikbommasandra						
1st Cross Rd	1	7.00	1.80	1.00	12.60	
2nd Cross Rd	1	4.70	1.80	1.00	8.46	
3rd Cross Rd	1	5.50	1.80	1.00	9.90	
4th Cross Rd	1	4.50	1.80	1.00	8.10	
Desilt						
Ambedkarnagara						
RHS(From 7th Main Rd)						
Ch:0.00m to 12.00m	1	12.00	0.80	0.70	6.72	
Ch:12.00m to 23.70m	1	11.70	0.80	0.70	6.55	
Ch:23.70m to 50.10m	1	26.40	0.80	0.70	14.78	
Ch:50.10m to 51.75m Gap	1	1.65				
Ch:51.75m to 81.75m	1	30.00	0.80	0.70	16.80	
Ch:81.75m to 83.75m	1	2.00	0.80	0.70	1.12	
Ch:83.75m to 95.55m Gap	1	11.80				
Ch:95.55m to 121.05m Gap	1	25.50				
Ch:121.05m to 141.05m	1	20.00	0.80	0.70	11.20	
Gap						
Ch:141.05m to 154.05m	1	13.00	0.80	0.70	7.28	
Gap						
Road Gap						
Ch:154.05m to 184.05m	1	30.00	0.80	0.70	16.80	
Ch:184.05m to 200.95m	1	16.90	0.80	0.70	9.46	
Road Gap						
Ch:200.95m to 229.95m	1	29.00	0.80	0.70	16.24	
Debris						
	1	4.00	2.00	0.30	2.40	
	1	6.80	4.00	0.40	10.88	
	1	5.00	3.10	0.30	4.65	
	1	6.00	3.00	0.40	7.20	
	1	4.00	3.90	0.30	4.68	
				Present Qty	**1120.11**	**Cum**
				Upto 125%	**1098.49**	**Cum**
				Above 125%	**21.62**	**Cum**

NEWZEN CONSULTANT Consultant

Asst. Engineer 28/12/2022

Asst. Exec. Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
h:50.10m to 51.75m	1	1.65				
h:51.75m to 81.75m	1	30.00	0.20	0.10	0.60	
h:81.75m to 83.75m	1	2.00	0.20	0.10	0.04	
h:83.75m to 95.55m	1	11.80	0.20	0.10	0.24	
h:95.55m to 121.05m	1	25.50	0.20	0.10	0.51	
h:121.05m to 141.05m	1	20.00	0.20	0.10	0.40	
Gap						
h:141.05m to 154.05m	1	13.00	0.20	0.10	0.26	
Gap						
Road Gap	1	4.00				
h:154.05m to 184.05m	1	30.00	0.20	0.10	0.60	
h:184.05m to 200.95m	1	16.90	0.20	0.10	0.34	
Road Gap	1	4.00				
h:200.95m to 229.95m	1	29.00	0.20	0.10	0.58	
For surround bench	10	6.40	0.20	0.10	1.28	
				Present Qty	**137.48**	**Cum**

NEWZEN CONSULTANT
Consultant

Asst. Engineer 4/01/2021

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು
Asst. Exec. Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Date of Pre-Measurement :

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. with 20mm and down size granite metal coarse aggregates at 0.69 cum and fine aggregates at 0.43 cum machine mixed, well compacted for walls and bottom including centering, shuttering, cost of materials, HOM of machinery, curing etc., complete excluding cost of steel as per MORTH specification No. 1500, 1700, 2200. including cost of materials, labour, HOM complete as per specificationsdo- Wall & bottom						
Raft						
Ambedkarnagara						
15th A cross Rd						
LHS(From Car Auto Spa)						
Ch:0.00m to 20.30m	1	20.30	1.20	0.20	4.87	
Ch:20.30m to 50.30m	1	30.00	1.20	0.20	7.20	
Ch:50.30m to 80.30m	1	30.00	1.20	0.20	7.20	
Ch:80.30m to 110.30m	1	30.00	1.20	0.20	7.20	
Ch:110.30m to 140.30m	1	30.00	1.20	0.20	7.20	
Ch:140.30m to 170.30m	1	30.00	1.20	0.20	7.20	
Ch:170.30m to 177.30m	1	7.00	1.20	0.20	1.68	
Road Gap						
Ch:177.30m to 204.40m	1	27.10				
Gap						
Ch:204.40m to 219.80m	1	15.40				
Gap						
Ch:219.80m to 241.80m	1	22.00				
Continue						
From (7th Main Rd)						
Ch:241.80m to 271.80m	1	30.00	1.20	0.20	7.20	
Ch:271.80m to 301.80m	1	30.00	1.20	0.20	7.20	
Ch:317.30m to 331.80m	1	30.00	1.20	0.20	7.20	
Chikbommasandra						
1st Main Rd						
RHS(From Main Rd)						
Ch:0.00m to 30.00m	1	30.00	1.50	0.20	9.00	
Culvert Gap						
Ch:30.00m to 51.00m	1	21.00	1.50	0.20	6.30	
Culvert Gap						
Ch:51.00m to 73.10m	1	22.10	1.50	0.20	6.63	
Culvert Gap						

NEWZEN CONSULTANTS Consultant Bangalore

Assistant Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು
Asst. Executive Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
h:73.10m to 100.60m	1	27.50	1.50	0.20	8.25	
ulvert Gap						
h:100.60m to 118.60m	1	18.00	1.50	0.20	5.40	
emple Road						
h:0.00m to 30.00m	1	30.00	1.50	0.20	9.00	
h:30.00m to 51.00m	1	21.00	1.50	0.20	6.30	
mbedkarnagara						
h:0.00m to 30.00m	1	30.00	0.90	0.15	4.05	
h:30.00m to 60.00m	1	30.00	0.90	0.15	4.05	
h:60.00m to 80.00m	1	20.00	0.90	0.15	2.70	
rain Wall						
mbedkarnagara						
6th A cross Rd						
HS(From Car Auto Spa)						
n:0.00m to 20.30m	2	20.30	0.23	0.80	7.47	
n:20.30m to 50.30m	2	30.00	0.23	0.80	11.04	
n:50.30m to 80.30m	2	30.00	0.23	0.80	11.04	
n:80.30m to 110.30m	2	30.00	0.23	0.80	11.04	
n:110.30m to 140.30m	2	30.00	0.23	0.80	11.04	
n:140.30m to 170.30m	2	30.00	0.23	0.80	11.04	
n:170.30m to 177.30m	2	7.00	0.23	0.80	2.58	
oad Gap						
n:177.30m to 204.40m	2	27.10				
ap						
n:204.40m to 219.80m	2	15.40				
ap						
n:219.80m to 241.80m	2	22.00				
ntinue						
om (7th Main Rd)						
n:241.80m to 271.80m	2	30.00	0.23	0.80	11.04	
n:271.80m to 301.80m	2	30.00	0.23	0.80	11.04	
n:317.30m to 331.80m	2	30.00	0.23	0.80	11.04	
nikbommasandra						
t Main Rd						
HS(From Main Rd)						
n:0.00m to 30.00m	2	30.00	0.25	0.90	13.50	
ulvert Gap						
n:30.00m to 51.00m	2	21.00	0.25	0.90	9.45	
ulvert Gap						
n:51.00m to 73.10m	2	22.10	0.25	0.90	9.95	
ulvert Gap						
n:73.10m to 100.60m	2	27.50	0.25	0.90	12.38	
ulvert Gap						

CITIZEN CONSULTANT Consultant

Ramesargouril
Assistant Engineer

Saulin
ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ನಗರಸಭೆ ಉಪವಿಭಾಗ,
ಬ ಬ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು
Asst. Executive Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
No of U-bar=727.00Nos	727	2.15		0.61	953.46	
Distribution bar						
Distribution bar 10mm dia @ 160mm						
0.61kg/mtr						
Culvert	13	80.00		0.61	634.40	
Total Culvert length=21.70m						
Main bar 12mm dia bar @ 120mm						
0.89kg/mtr, Double mat						
No of U-bar=363.00Nos						
Distribution bar	363	3.30		0.89	1066.13	
Distribution bar 10mm dia @200mm						
0.61kg/mtr, Double mat						
	32	21.70		0.61	423.58	
					31880.07	Kgs
				Present Qty	**31.88**	**Ton**

NEWZEN CONSULTANTS
Consultant

Assistant Engineer 11/01/2021

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ/Assistant Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
19	KSRRB M300-53. Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300-2 complete as per specifications, including cost of gravel / murrum, watering charges & compaction by vibratory roller to 95% of modified proctors density. MORTH Specification No 305						
	For Benches	10	1.50	1.80	0.20	5.40	Cum
					Present Qty	**5.40**	**Cum**

Contractor

NEWZEN CONSULTANT Bangalore Consultant

Asst. Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Sl No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
1	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, including cost of all materials, labour, HOM curing complete as per specifications. Specification						
	Ambedkarnagara						
	15th A cross Rd						
	LHS(Dead End)						
	Ch:0.00m to 2.90m	2	2.90	0.20	0.15	0.17	
	Ch:0.00m to 3.10m	2	3.10	0.20	0.15	0.19	
	Ch:0.00m to 3.50m	2	3.50	0.20	0.15	0.21	
	Ch:0.00m to 3.50m	2	3.50	0.20	0.15	0.21	
	Ch:0.00m to 3.20m	2	3.20	0.20	0.15	0.19	
	Ch:0.00m to 2.55m	2	2.55	0.20	0.15	0.15	
	Ch:0.00m to 3.40m	2	3.40	0.20	0.15	0.20	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 3.05m	2	3.05	0.20	0.15	0.18	
	Ch:0.00m to 2.95m	2	2.95	0.20	0.15	0.18	
	Ch:0.00m to 3.10m	2	3.10	0.20	0.15	0.19	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 3.40m	2	3.40	0.20	0.15	0.20	
	Ch:0.00m to 2.70m	2	2.70	0.20	0.15	0.16	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 4.00m	2	4.00	0.20	0.15	0.24	
	Ch:0.00m to 2.50m	2	2.50	0.20	0.15	0.15	
	Ch:0.00m to 2.50m	2	2.50	0.20	0.15	0.15	
	Ch:0.00m to 2.50m	2	2.50	0.20	0.15	0.15	
	Ch:0.00m to 3.30m	2	3.30	0.20	0.15	0.20	
	Ch:0.00m to 3.20m	2	3.20	0.20	0.15	0.19	
	Ch:0.00m to 2.40m	2	2.40	0.20	0.15	0.14	
	Ch:0.00m to 2.20m	2	2.20	0.20	0.15	0.13	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 3.60m	2	3.60	0.20	0.15	0.22	
	Ch:0.00m to 2.00m	2	2.00	0.20	0.15	0.12	

tractor

NEWZEN CONSULTANT Consultant Bangalore

Asst. Engineer

8/02/2022

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
Asst. Executive Engineer,
ಬ.ಬ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-560064

JYOTHI NAGARA,
080 23240187

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit
	Ch:0.00m to 2.10m	2	2.10	0.20	0.15	0.13	
	Ch:0.00m to 2.00m	2	2.00	0.20	0.15	0.12	
	Ch:0.00m to 2.00m	2	2.00	0.20	0.15	0.12	
	Ch:0.00m to 2.60m	2	2.60	0.20	0.15	0.16	
	Ch:0.00m to 2.10m	2	2.10	0.20	0.15	0.13	
	Shoulder Drain Bed						
	LHS(Dead End)						
	Ch:0.00m to 1.90m	1	1.90	0.60	0.15	0.17	
	Ch:0.00m to 2.10m	1	2.10	0.60	0.15	0.19	
	Ch:0.00m to 2.00m	1	2.00	0.60	0.15	0.18	
	Ch:0.00m to 1.90m	1	1.90	0.60	0.15	0.17	
	Ch:0.00m to 1.90m	1	1.90	0.60	0.15	0.17	
	Ch:0.00m to 2.00m	1	2.00	0.60	0.15	0.18	
	Ch:0.00m to 2.00m	1	2.00	0.60	0.15	0.18	
	Ch:0.00m to 1.90m	1	1.90	0.60	0.15	0.17	
	RHS(From 7th Main Rd)						
	Ch:0.00m to 2.60m	1	2.60	0.60	0.15	0.23	
	Ch:0.00m to 2.40m	1	2.40	0.60	0.15	0.22	
	Ch:0.00m to 2.40m	1	2.40	0.60	0.15	0.22	
	Ch:0.00m to 1.90m	1	1.90	0.60	0.15	0.17	
	Ch:0.00m to 2.10m	1	2.10	0.60	0.15	0.19	
	Ch:0.00m to 2.00m	1	2.00	0.60	0.15	0.18	
	Ch:0.00m to 2.00m	1	2.00	0.60	0.15	0.18	
	Ch:0.00m to 2.60m	1	2.60	0.60	0.15	0.23	
	Ch:0.00m to 2.10m	1	2.10	0.60	0.15	0.19	
					Present Qty	**13.53**	**Sqm**

ntractor

NEWZEN CONSULTANT Consultant

Ramadangrenzil

Asst. Engineer

8/02/

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು

Asst. Exec. Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
Ch:0.00m to 2.00m	2	2.00		0.20	0.80	
Ch:0.00m to 2.60m	2	2.60		0.20	1.04	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 2.40m	2	2.40		0.20	0.96	
Ch:0.00m to 2.10m	2	2.10		0.20	0.84	
Ch:0.00m to 1.70m	2	1.70		0.20	0.68	
Ch:0.00m to 2.70m	2	2.70		0.20	1.08	
Ch:0.00m to 2.40m	2	2.40		0.20	0.96	
Ch:0.00m to 3.40m	2	3.40		0.20	1.36	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 2.00m	2	2.00		0.20	0.80	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 2.40m	2	2.40		0.20	0.96	
Ch:0.00m to 1.80m	2	1.80		0.20	0.72	
Ch:0.00m to 2.00m	2	2.00		0.20	0.80	
Ch:0.00m to 1.80m	2	1.80		0.20	0.72	
Ch:0.00m to 1.80m	2	1.80		0.20	0.72	
RHS(From 7th Main Rd)						
Ch:0.00m to 1.90m	2	1.90		0.40	1.52	
Ch:0.00m to 3.40m	2	3.40		0.40	2.72	
Ch:0.00m to 1.70m	2	1.70		0.20	0.68	
Ch:0.00m to 1.20m	2	1.20		0.20	0.48	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 1.20m	1	1.20		0.20	0.24	
Ch:0.00m to 2.70m	2	2.70		0.20	1.08	
Ch:0.00m to 2.80m	2	2.80		0.20	1.12	
Shoulder Drain						
LHS(Dead End)						
Ch:0.00m to 1.90m	2	1.90		0.40	1.52	
Ch:0.00m to 2.10m	2	2.10		0.40	1.68	
Ch:0.00m to 2.00m	2	2.00		0.20	0.80	
Ch:0.00m to 1.90m	2	1.90		0.20	0.76	
Ch:0.00m to 1.90m	2	1.90		0.40	1.52	
Ch:0.00m to 2.00m	2	2.00		0.40	1.60	
Ch:0.00m to 2.00m	2	2.00		0.40	1.60	
Ch:0.00m to 1.90m	2	1.90		0.40	1.52	
RHS(From 7th Main Rd)						
Ch:0.00m to 2.60m	2	2.60		0.40	2.08	
Ch:0.00m to 2.40m	2	2.40		0.40	1.92	
Ch:0.00m to 2.40m	2	2.40		0.40	1.92	
Ch:0.00m to 1.90m	2	1.90		0.40	1.52	

ctor

NEWZEN CONSULTANT Consultant Bangalore

Ramarangeevi

Asst. Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಧಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ.ಬೆಂಗಳೂರು-106
Asst. Exec. Engineer

Discription of Item	No	Length	Breadth	Depth	Qty	Unit
Ch:0.00m to 2.10m	2	2.10		0.40	1.68	
Ch:0.00m to 2.00m	2	2.00		0.40	1.60	
Ch:0.00m to 2.00m	2	2.00		0.20	0.80	
Ch:0.00m to 2.60m	2	2.60		0.40	2.08	
Ch:0.00m to 2.10m	2	2.10		0.20	0.84	
				Present Qty	**81.98**	**Sqm**

ractor

NEWZEN CONSULTANT Consultant Bangalore

Asst. Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬ ಬ.ಎಂ.ಪಿ ಬೆಂಗಳೂರು-106
Asst. Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
KSRRB 300-1 Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications								
Vide Premeasurement page no.					1098.49			
				Present Qty	**1098.49**	**Cum**	**225.94**	**248193.00**
KSRB 4-1 2 Providing and laying in position plain cement concrete of Mix 1 3 6 with OPC @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0 892cum and fine aggregates @ 0 465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms thick, well compacted, in foundation including cost of all materials, labour, HOM curing complete as per specifications								
Vide Premeasurement page no.					137 48			
				Present Qty	**137.48**	**Cum**	**5690.28**	**299198.00**
Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. with 20mm and down size granite metal coarse aggregates at 0 69 cum and fine aggregates at 0 43 cum machine mixed, well compacted for walls and bottom including centering, shuttering, cost of materials, HOM of machinery, curing etc., complete excluding cost of steel as per MORTH specification No. 1500, 1700, 2200 including cost of materials, labour, HOM complete as per specifications								
Vide Premeasurement page no.					340 74			
				Present Qty	**340.74**	**Cum**	**7420.17**	**2528328.00**
KSRRB M2200-6 Providing T.M.T. steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per disign (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM complete as per specification.								
Vide Premeasurement page no.					31 88			
				Present Qty	**31.88**	**Tn**	**77654.86**	**2475643.00**
KSRRB M300-53 Construction of embankment with approved material Gravel/Murrum with all lifts and leads, transporting to site, spreading, grading to required slope and compacting to meet requirement Table 300-2 complete as per specifications, including cost of gravel / murrum, watering charges & compaction by vibratory roller to 95% of modified proctors density. MORTH Specification No. 305								
Vide Premeasurement page no.					5.40			
				Present Qty	**5.40**	**Cum**	**361.55**	**1953.00**
Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work site, spreading in uniform layers with motor grader on prepared surface and compacting with vibratory power roller to achieve the 98 % proctor density, complete as per specifications								
Vide Premeasurement page no.					481 60			
				Present Qty	**481.60**	**Cum**	**2094.47**	**1008694.00**
EIRL								
SRB 4-1 2 Providing and laying in position plain cement concrete of Mix 1 3 6 with OPC @ 20kgs, with 40mm and down size graded granite metal coarse aggregates @0 892cum and fine ggregates @ 0 465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 ms thick, well compacted, in foundation including cost of all materials, labour, HOM curing mplete as per specifications								
ide Premeasurement page no.					13 53			
				Present Qty	**13.53**	**Cum**	**6031.81**	**81629.00**

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
KSRB 5-14 Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not lessthan 1800 kg/m3 and having a minimum average compressive strength 4 00 N/mm2 confirming to IS 2185 (Part) 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charegs, scaffolding, curing complete as per specifications.								
Vide Premeasurement page no.					81 98			
				Present Qty	**81.98**	**Sqm**	**1027.92**	**84270.00**

Contractor

NEWIZEN CONSULTANT Consultant Bangalore

Assistant Engineer

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

Asst. Executive Engineer

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Shivanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Providing and Fixing pre cast covering Slab 100mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc								
Ambedkarnagara								
15th A cross Rd								
LHS(From Car Auto Spa)								
Ch:0.00m to 20.30m	1	20.30	0.00		0.00			
Ch:20.30m to 50.30m	1	30.00	1.20		36.00			
Ch:50.30m to 80.30m	1	30.00	1.20		36.00			
Ch:80.30m to 110.30m	1	30.00	1.20		36.00			
Ch:110.30m to 140.30m	1	30.00	1.20		36.00			
Ch:140.30m to 170.30m	1	30.00	1.20		36.00			
Ch:170.30m to 177.30m	1	7.00	1.20		8.40			
Road Gap								
Ch:177.30m to 204.40m	1	27.10						
Gap								
Ch:204.40m to 219.80m	1	15.40						
Gap								
Ch:219.80m to 241.80m	1	22.00						
Continue								
From (7th Main Rd)								
Ch:241.80m to 271.80m	1	30.00	1.20		36.00			
Ch:271.80m to 301.80m	1	30.00	1.20		36.00			
Ch:317.30m to 331.80m	1	30.00	1.20		36.00			
Ambedkarnagara								
LHS(From 7th Main Rd)								
Ch:0.00m to 12.00m	1	12.00	1.20		14.40			
Ch:12.00m to 23.70m	1	11.70	0.00		0.00			
Ch:23.70m to 50.10m	1	26.40	1.20		31.68			
Ch:50.10m to 51.75m Gap	1	1.65						
Ch:51.75m to 81.75m	1	30.00	1.20		36.00			
Ch:81.75m to 83.75m	1	2.00	1.20		2.40			
Ch:83.75m to 95.55m Gap	1	11.80						
Ch:95.55m to 121.05m Gap	1	25.50						
Ch:121.05m to 141.05m	1	20.00	1.20		24.00			
Gap								

NEWZEN CONSULTANT Consultant Bangalore

Ramesh Jeeral
Asst. Engineer 17/02/2022

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106
Asst. Exec. Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Ch:141.05m to 154.05m	1	13.00	1.20		15.60			
Gap								
Road Gap								
Ch:154.05m to 184.05m	1	30.00	1.20		36.00			
Ch:184.05m to 200.95m	1	16.90	1.20		20.28			
Road Gap								
Ch:200.95m to 229.95m	1	29.00	1.20		34.80			
Deduct BS Slab	-6	0.60	1.20		-4.32			
Ambedkarnagara								
Ch:0.00m to 26.00m	1	26.00	0.90		23.40			
Gap								
Ch:26.00m to 41.40m	1	15.40	0.90		13.86			
Gap								
Ch:41.40.00m to 63.40m	1	22.00	0.90		19.80			
Shoulder Drain								
LHS(Dead End)								
Ch:0.00m to 1.90m	1	1.90	0.75		1.43			
Ch:0.00m to 2.10m	1	2.10	0.75		1.58			
Ch:0.00m to 2.00m	1	2.00	0.75		1.50			
Ch:0.00m to 1.90m	1	1.90	0.75		1.43			
Ch:0.00m to 2.00m	1	2.00	0.75		1.50			
Ch:0.00m to 2.00m	1	2.00	0.75		1.50			
Ch:0.00m to 1.90m	1	1.90	0.75		1.43			
RHS(From 7th Main Rd)								
Ch:0.00m to 2.60m	1	2.60	0.75		1.95			
Ch:0.00m to 2.40m	1	2.40	0.75		1.80			
Ch:0.00m to 2.40m	1	2.40	0.75		1.80			
Ch:0.00m to 1.90m	1	2.00	0.75		1.50			
Ch:0.00m to 2.10m	1	2.10	0.75		1.58			
Ch:0.00m to 2.00m	1	2.00	0.75		1.50			
Ch:0.00m to 2.00m	1	2.00	0.75		1.50			
Ch:0.00m to 2.60m	1	2.60	0.75		1.95			
Ch:0.00m to 2.10m	1	2.10	0.75		1.58			
MISSING SLABS								
Ambedkarnagara								
6th Cross Rd								
	1	8.00	0.90		7.20			
	1	12.00	0.90		10.80			
	1	13.00	0.90		11.70			
	1	10.00	0.90		9.00			
	1	9.00	0.90		8.10			
	1	10.00	0.90		9.00			

08/03/2024

NEWZEN CONSULTANTS Consultant Bangalore

Ramanjaneyulu

Asst. Engineer 17/02/2024

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-560

Asst. Exec. Engineer,



Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
	1	11.00	0.90		9.90			
1st Main Rd	1	10.00	0.90		9.00			
	1	14.00	0.90		12.60			
	1	12.00	0.90		10.80			
	1	9.00	0.90		8.10			
	1	14.00	0.90		12.60			
	1	13.00	0.90		11.70			
	1	9.00	0.90		8.10			
	1	10.00	0.90		9.00			
	1	9.00	0.90		8.10			
15th A cross Rd	1	9.00	0.90		8.10			
	1	10.00	1.20		12.00			
	1	7.60	1.20		9.12			
	1	7.00	1.20		8.40			
	1	8.00	1.20		9.60			
	1	7.00	1.20		8.40			
	1	8.00	1.20		9.60			
	1	10.00	1.20		12.00			
Present Qty					**824.22**	**Sqm**		
Upto 125%					**626.25**	**Sqm**	**2452.68**	**1535991.00**
Above 125%					**197.97**	**Sqm**	**2452.68**	**485558.00**

NEWZEN CONSULTANTS Bangalore Consultant

Ramaganjeeveh

Asst. Engineer 17/02/2021

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ.
ಜ ಜ.ಎಂ.ಕಾವೇರಿಪುರ-106.

Exec. Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Providing and Fixing pre cast covering Slab 150mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc								
Chikbommasandra								
1st Main Rd								
RHS(From Main Rd)								
Ch:0.00m to 30.00m	1	18.00	1.50		27.00			
Culvert Gap								
Ch:30.00m to 51.00m	1	21.00	1.50		31.50			
Culvert Gap								
Ch:51.00m to 73.10m	1	22.10	1.50		33.15			
Culvert Gap								
Ch:73.10m to 100.60m	1	27.50	1.50		41.25			
Culvert Gap								
Ch:100.60m to 118.60m	1	18.00	1.50		27.00			
Deduct BS Slab	-10	0.60	1.50		-9.00			
Temple Road								
Ch:0.00m to 30.00m	1	30.00	1.50		45.00			
Ch:30.00m to 51.00m	1	21.00	1.50		31.50			
				Present Qty	**227.40**	**Sqm**	**2616.40**	**594970.00**

NEWZEN CONSULTANTS Bangalore Consultant

Ramasanjeeva L

Asst. Engineer

20/02/2

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು

Asst. Exec. Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Ganganagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Date of Measurement :

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
15	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading,								
	RCC Culvert								
	Chikbommasandra								
	1st Cross Rd	1	7.00	1.50		10.50			
	2nd Cross Rd	1	4.70	1.50		7.05			
	3rd Cross Rd	1	5.50	1.50		8.25			
	4th Cross Rd	1	4.50	1.50		6.75			
	Culvert Slab								
	Chikbommasandra								
	1st Main Rd								
	RHS(From Main Rd)								
	Ch 0.00m to 12.60m	1	12.60	1.50		18.90			
					Present Qty	**51.45**	**Sqm**		
					Upto 125%	**9.00**	**Sqm**	**5686.19**	**51176.00**
					Above 125%	**42.45**	**Sqm**	**5686.19**	**241379.00**

NEWZEN CONSULTANT Bangalore Consultant

Assistant Engineer 23/02/2029

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
Asst. Executive Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including cost of materials, labour charges of machinery, loading and unloading, lead and lift,								
Ambedkarnagara								
15th A cross Rd								
LHS(From Car Auto Spa)								
Ch:0.00m to 20.30m	1	20.30			20.30			
Ch:20.30m to 50.30m	1	30.00			30.00			
Ch:50.30m to 80.30m	1	30.00			30.00			
Ch:80.30m to 110.30m	1	30.00			30.00			
Ch:110.30m to 140.30m	1	30.00			30.00			
Ch:140.30m to 170.30m	1	30.00			30.00			
Ch:170.30m to 177.30m	1	7.00			7.00			
Road Gap								
Ch:177.30m to 204.40m	1	27.10			27.10			
Gap								
Ch:204.40m to 219.80m	1	15.40			15.40			
Gap								
Ch:219.80m to 241.80m	1	22.00			22.00			
Continue								
From (7th Main Rd)								
Ch:241.80m to 271.80m	1	30.00			30.00			
Ch:271.80m to 301.80m	1	30.00			30.00			
Ch:317.30m to 331.80m	1	30.00			30.00			
Ambedkarnagara								
RHS(From 7th Main Rd)								
Ch:0.00m to 12.00m	1	12.00			12.00			
Ch:12.00m to 23.70m	1	11.70			11.70			
Ch:23.70m to 50.10m	1	26.40			26.40			
Ch:50.10m to 51.75m	1	1.65						
Ch:51.75m to 81.75m	1	30.00			30.00			
Ch:81.75m to 83.75m	1	2.00			2.00			
Ch:83.75m to 95.55m	1	11.80			11.80			
Ch:95.55m to 121.05m	1	25.50			25.50			

08/05/2021

Consultant

Asst. Engineer 26/02/2021

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-064

Asst. Exec. Engineer,

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Ch:121.05m to 141.05m	1	20.00			20.00			
Gap								
Ch:141.05m to 154.05m	1	13.00			13.00			
Gap								
Road Gap	1	4.00						
Ch:154.05m to 184.05m	1	30.00			30.00			
Ch:184.05m to 200.95m	1	16.90			16.90			
Road Gap		4.00						
Ch:200.95m to 229.95m	1	29.00			29.00			
For surround bench	10	6.40			64.00			
					624.10	**M**		
				Present Qty	**1387.00**	**Nos**	**453.89**	**629546.00**

NEWZEN CONSULTANTS Consultant Bangalore

Asst. Engineer 28/02/2022

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

Asst. Engineer,

ame of Work: Improvements to roads and Drains at Ambedkarnagara and nakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

rement Recorded On:

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
ainting two coats after filling the surface with synthetic enamel paint in pproved shades on new plastered concrete surfaces, with materials, labour mplete as per specifications. MORTH Chapter 8 Specification No. SRRB M800-6. (P.No.180, I.No.24.1 of PW, P&IWTD SR 2018-19)								
mbedkarnagara								
5th A cross Rd								
HS(From Car Auto Spa)								
h:0.00m to 20.30m	1	20.30		0.30	6.09			
h:20.30m to 50.30m	1	30.00		0.30	9.00			
n:50.30m to 80.30m	1	30.00		0.30	9.00			
n:80.30m to 110.30m	1	30.00		0.30	9.00			
n:110.30m to 140.30m	1	30.00		0.30	9.00			
n:140.30m to 170.30m	1	30.00		0.30	9.00			
n:170.30m to 177.30m	1	7.00		0.30	2.10			
oad Gap								
n:177.30m to 204.40m	1	27.10		0.30	8.13			
ap								
:204.40m to 219.80m	1	15.40		0.30	4.62			
ap								
:219.80m to 241.80m	1	22.00		0.30	6.60			
ntinue								
om (7th Main Rd)								
:241.80m to 271.80m	1	30.00		0.30	9.00			
:271.80m to 301.80m	1	30.00		0.30	9.00			
:317.30m to 331.80m	1	30.00		0.30	9.00			
bedkarnagara								
IS(From 7th Main Rd)								
:0.00m to 12.00m	1	12.00		0.30	3.60			
:12.00m to 23.70m	1	11.70		0.30	3.51			
23.70m to 50.10m	1	26.40		0.30	7.92			
:50.10m to 51.75m	1	1.65						
:51.75m to 81.75m	1	30.00		0.30	9.00			
:81.75m to 83.75m	1	2.00		0.30	0.60			
83.75m to 95.55m	1	11.80		0.30	3.54			
95.55m to 121.05m	1	25.50		0.30	7.65			
121.05m to 141.05m	1	20.00		0.30	6.00			

NEWZEN CONSULTANT Consultant Bangalore

Asst. Engineer 6/03/2021

Asst. Exec. Engineer, ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ, ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು

Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
Gap								
Ch 141.05m to 154.05m	1	13.00		0.30	3.90			
Gap								
Road Gap	1	4.00						
Ch 154.05m to 184.05m	1	30.00		0.30	9.00			
Ch 184.05m to 200.95m	1	16.90		0.30	5.07			
Road Gap	1	4.00						
Ch 200.95m to 229.95m	1	29.00		0.30	8.70			
For surround bench	10	6.40		0.30	19.20			
				Present Qty	**187.23**	**Sqm**	**89.00**	**16664.00**

NEWZEN CONSULTANT Bangalore Consultant

Asst. Engineer 6/03/2021

ಪಕಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಧಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬ.ಬ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು

Asst. Executive Engineer,

Name of Work: Improvements to roads and Drains at Ambedkarnagara and Kanakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division

Detailed Measurements

Measurement Recorded On:

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
18	Providing and laying/fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick for flooring conforming to IS 1237 heavy duty tiles for flooring, treads of steps and landing, laid on a bed of 12mm thick cement mortar 1:3 mis finished with flush pointing using white cement, including cost of materials, mortar, including cutting, griding the edge to half/full round wherever required, labour, curing complete as per specification.								
	For Benches	10	1.50	1.80		27.00			
					Present Qty	**27.00**	**Sqm**	**1370.56**	**37006.00**

NEWZEN CONSULTANTS Bangalore Consultant

Asst. Engineer

Exec. Engineer,

Name of Work: **Improvements to roads and Drains at Ambedkarnagara and Basavakanagara areas in ward no-04 of Yelahanka Satellite Town Sub Division**

Detailed Measurements

Measurement Recorded On:

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
22	KSRB 14.6 : Providing and laying heavy duty cobble stones interlock pavers, using cement and course sand for manufacture of blocks of approved size, shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed (average thickness) and compacting with plate vibrator having 3 tons compaction force thereby forcing part of sand underneath to come up in between joints, final compaction of paver surface joints into its final level, including cost of materials, labour and HOM complete as								
	Ambedkarnagara								
	15th A cross Rd								
	LHS(From Car Auto Spa)								
	Ch:0.00m to 20.30m	1	20.30	1.90		38.57			
	Ch:20.30m to 50.30m	1	30.00	1.80		54.00			
	Ch:50.30m to 80.30m	1	30.00	1.90		57.00			
	Ch:80.30m to 110.30m	1	30.00	1.80		54.00			
	Ch:110.30m to 140.30m	1	30.00	1.80		54.00			
	Ch:140.30m to 170.30m	1	30.00	1.80		54.00			
	Ch:170.30m to 177.30m	1	7.00	1.80		12.60			
	Road Gap								
	Ch:177.30m to 204.40m	1	27.10	2.20		59.62			
	Gap								
	Ch:204.40m to 219.80m	1	15.40	2.30		35.42			
	Gap								
	Ch:219.80m to 241.80m	1	22.00	2.40		52.80			
	Continue								
	From (7th Main Rd)								
	Ch:241.80m to 271.80m	1	30.00	1.80		54.00			
	Ch:271.80m to 301.80m	1	30.00	1.80		54.00			
	Ch:317.30m to 331.80m	1	30.00	1.80		54.00			
	Deduct Tree Guards	-48	1.10	1.00		-52.80			
	Ambedkarnagara								
	RHS(From 7th Main Rd)								
	Ch:0.00m to 12.00m	1	12.00	2.30		27.60			
	Ch:12.00m to 23.70m	1	11.70	2.00		23.40			
	Ch:23.70m to 50.10m	1	26.40	2.00		52.80			
	Ch:50.10m to 51.75m	1	1.65						
	Ch:51.75m to 81.75m	1	30.00	2.10		63.00			

Contractor

NEMZEN CONSULTANTS Consultant

Ramesangeeredi

Asst. Engineer 3/04/2021

ಸಹಾಯಕ ಕಾರ್ಯ ಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು
Asst. Exec. Engineer,

Item No	Discription of Item	No	Length	Breadth	Depth	Qty	Unit	Rate	Amount
	Ch:81.75m to 83.75m	1	2.00	2.10		4.20			
	Ch:83.75m to 95.55m	1	11.80	2.10		24.78			
	Ch:95.55m to 121.05m	1	25.50						
	Ch:121.05m to 141.05m	1	20.00	2.10		42.00			
	Gap								
	Ch:141.05m to 154.05m	1	13.00	2.10		27.30			
	Gap								
	Road Gap	1	4.00						
	Ch:154.05m to 184.05m	1	30.00	2.20		66.00			
	Ch:184.05m to 200.95m	1	16.90	2.10		35.49			
	Road Gap	1	4.00						
	Ch:200.95m to 229.95m	1	29.00	2.20		63.80			
	Deduct Tree Guards	-8	1.00	0.80		-6.40			
					Present Qty	**1005.18**	**Sqm**	**1171.43**	**1177499.00**
						Total			**11483652.00**
						GST 12%			
						Grand Total			

Contractor

NEWZEN CONSULTANT Bangalore Consultant

Asst. Engineer 3/04/202

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ.ಬೆಂಗಳೂರು-106.
Exec. Engineer,

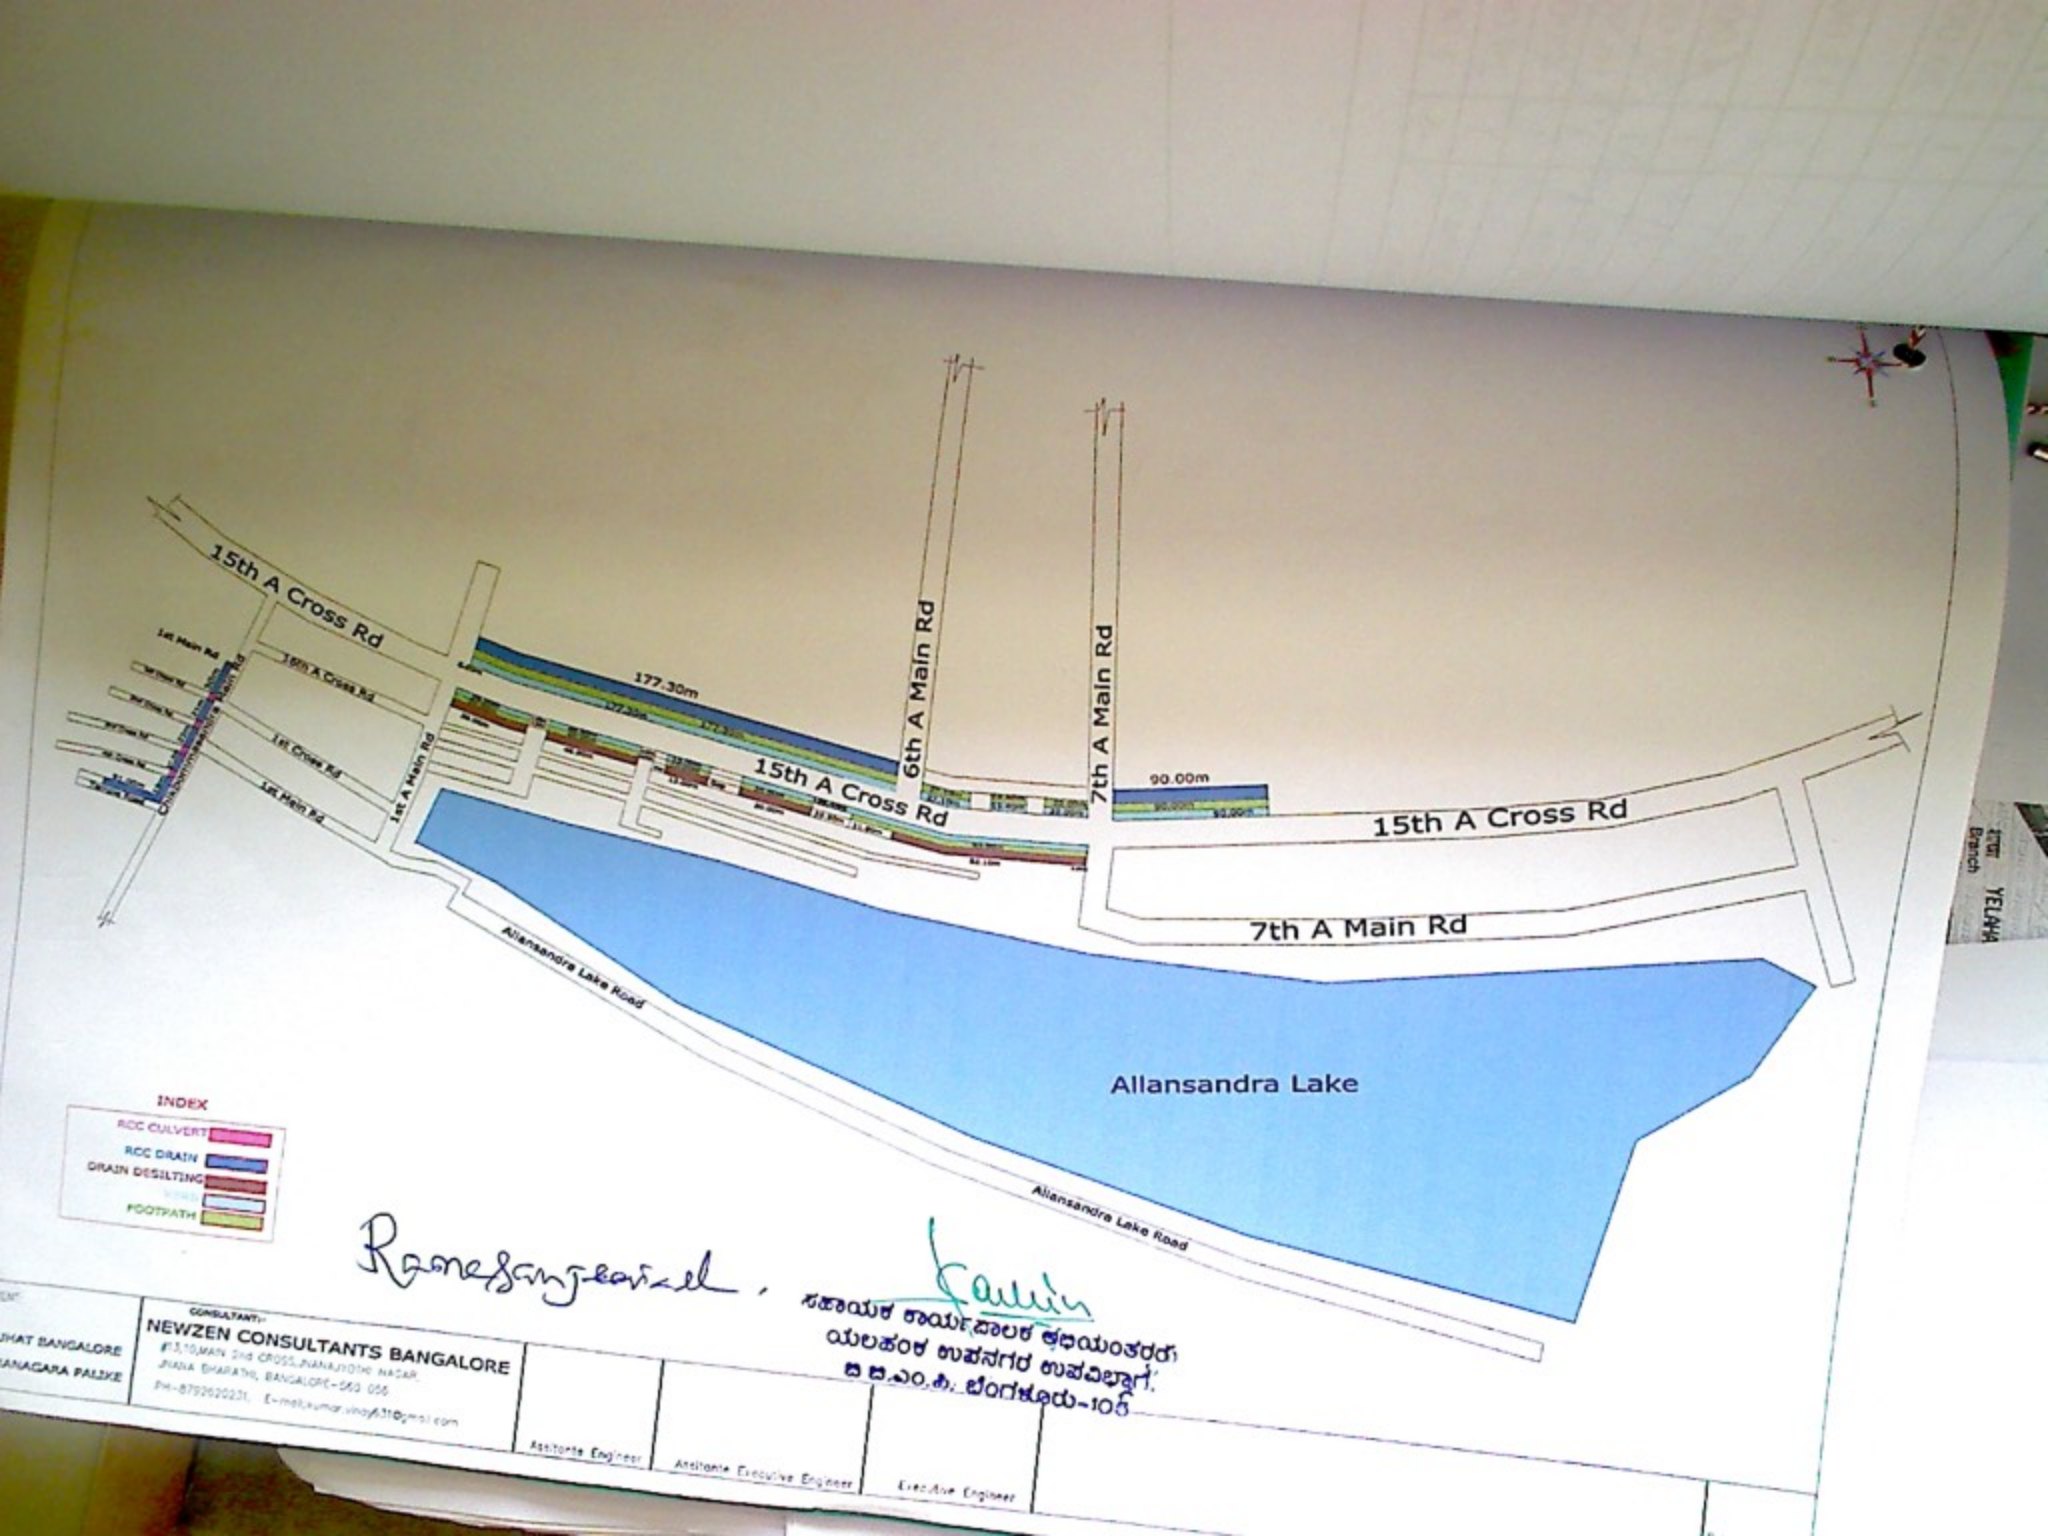

Ramesangeeth.

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ,
ಬ.ಬ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-106
